



TKC Portfolio & Resource Utilization Dashboard

Update By: Nuntawan Phoonkerd
Update Date: 27-04-2026



TKC Portfolio and Resource Utilization Dashboard



1. Objective :

Act as a centralized hub for consolidating and communicating project updates within TKC and resource utilization to both executives and team members.

2. Work areas:

- 01 Executive Summary
- 02 Overall Project Performance
- 03 Project Health

TKC Portfolio Dashboard



01 EXECUTIVE SUMMARY

TKC

Total Projects 2026

4/10

Active/ All Project in 2026

Proj. Value vs Target 2026

94%

of target



Value 284M / Target 302M
Remaining 18M

Billed vs Project Value

70%

of target



Billed 198M / Value 284M
Remaining 86M

Budget Burn Rate

73%


of target




Expensed 142M / Budget 195M
Remaining 53M

02 OVERALL PROJECT PERFORMANCE

Overall by Status

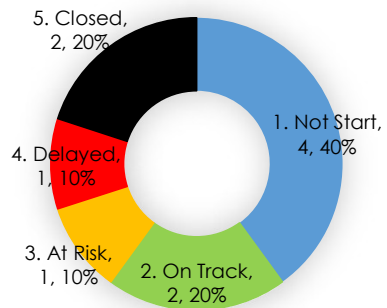

Instalment Payments Timeline — by Project by Month (B&M and Exc. VAT)

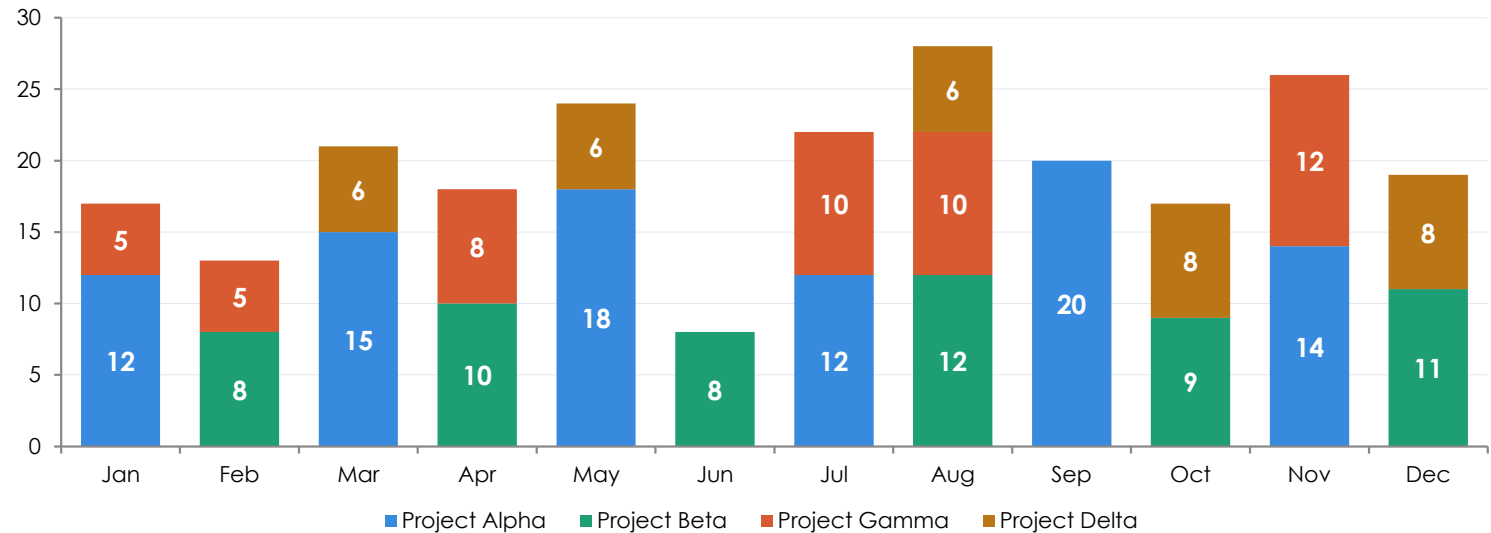

Project Alpha

PM: Nuntawan Phoonkerd
Updated Date : 30/03/2026 (No any update 30 days)
Click here : [Project Document](#)

On Track

PY 2025

Overall Progress

78%

Project Timeline

15/01/2025

Today (30/04/2026)

30/06/2026

Click here: [Project Timeline](#)

Resource Utilization

Plan

240

Actual (82%)

197

Financing (Exc. VAT)

Project Cost

85M

Billed (76%)



65M

Budget

60M

Expensed (85%)

51M

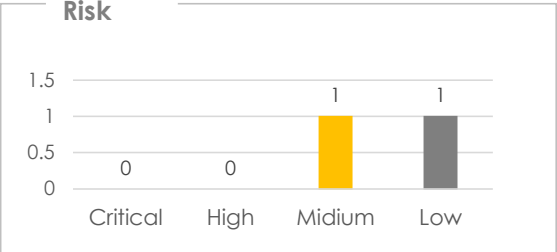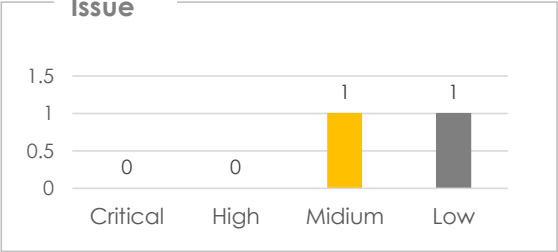

Term	Due Date		Amount (Exc.VAT)	Billed Status
	Original	Revised		
1	07/05/2025		15,000,000	✓
2	06/07/2026		15,000,000	✓
3	03/12/2025		15,000,000	✓
4	30/03/2026		20,000,000	✓
5	30/06/2026		20,000,000	⚠ Within 60 days

Click here : [Project Issue & Risk Logs](#)

Project Beta

PM: Nuntawan Phoonkerd
Updated Date : 30/03/2026 (No any update 30 days)
Click here : [Project Document](#)

Delay

PY 2026

Overall Progress

35%

Project Timeline

15/01/2026

Today (30/04/2026)

30/06/2027

Click here: [Project Timeline](#)

Resource Utilization

Plan

200

Actual (125%)

250

Financing (Exc. VAT)

Project Cost

63M

Billed (15%)

10M

Budget

38M

Expensed (105%)

40M

Issue

4

3

2

1

0

0

3

1

1

Critical

High

Midium

Low

Risk

4

3

2

1

0

0

3

1

1

Critical

High

Midium

Low

Click here : [Project Issue & Risk Logs](#)

Term	Due Date		Amount (Exc.VAT)	Billed Status
	Original	Revised		
1	30/01/2026		10,000,000	✓
2	30/03/2026	30/04/2026	10,000,000	⚠ Over 30 days
3	30/12/2026		15,000,000	
4	30/03/2027		15,000,000	
5	30/06/2027		13,000,000	

TKC Resource Utilization Dashboard



All Employee > All Roles

Name	Apr,2026				May,2026			
	06	13	20	23 (Today)	04	11	18	25
Nuntawan.P (June) • PM	120% (48/40) • PJ = 48 Hrs. (OT=8) • Non-PJ = 0 Hrs. Project Alpha Project Beta	100% (40/40) • PJ = 20 Hrs. • Non-PJ = 20 Hrs. Project Alpha	55% (22/40) • PJ = 22 Hrs. (OT=2) • Non-PJ = 0 Hrs. Project Alpha	0% (0/48) • PJ = 0/48 Hrs. • Non-PJ = 0 Hrs. Project Alpha	0% (0/48) • PJ = 0/48 Hrs. • Non-PJ = 0 Hrs. Project Alpha	0% (0/40) • PJ = 0/40 Hrs. • Non-PJ = 0 Hrs. Project Alpha	0% (0/40) • PJ = 0/40 Hrs. • Non-PJ = 0 Hrs. Project Alpha	0% (0/40) • PJ = 0/40 Hrs. • Non-PJ = 0 Hrs. Project Alpha
ABC DEF (A) • PM	100% (40/40) • PJ = 0 Hrs. • Non-PJ = 40 Hrs. Project Beta	100% (40/40) • PJ = 40 Hrs. • Non-PJ = 0 Hrs. Project Beta	100% (40/40) • PJ = 40 Hrs. • Non-PJ = 0 Hrs. Project Beta	50% (0/40) • PJ = 20/40 Hrs. • Non-PJ = 0 Hrs. Project Beta	0% (0/40) • PJ = 0/40 Hrs. • Non-PJ = 0 Hrs. Project Beta	0% (0/0) • PJ = 0/0 Hrs. • Non-PJ = 0 Hrs.	0% (0/0) • PJ = 0/0 Hrs. • Non-PJ = 0 Hrs.	0% (0/0) • PJ = 0/0 Hrs. • Non-PJ = 0 Hrs.
GHI JKL (G) • SW Eng.	0% (0/0) • PJ = 0/0 Hrs. • Non-PJ = 0 Hrs.	0% (0/0) • PJ = 0/0 Hrs. • Non-PJ = 0 Hrs.	0% (0/0) • PJ = 0/0 Hrs. • Non-PJ = 0 Hrs.	0% (0/0) • PJ = 0/0 Hrs. • Non-PJ = 0 Hrs.	0% (0/0) • PJ = 0/0 Hrs. • Non-PJ = 0 Hrs.	0% (0/0) • PJ = 0/0 Hrs. • Non-PJ = 0 Hrs.	0% (0/0) • PJ = 0/0 Hrs. • Non-PJ = 0 Hrs.	0% (0/0) • PJ = 0/0 Hrs. • Non-PJ = 0 Hrs.
MNO PQR (M) • SW Eng.					0% (0/40) • PJ = 0/40 Hrs. • Non-PJ = 0 Hrs. Project Alpha	0% (0/40) • PJ = 0/40 Hrs. • Non-PJ = 0 Hrs. Project Alpha	0% (0/40) • PJ = 0/40 Hrs. • Non-PJ = 0 Hrs. Project Alpha	0% (0/40) • PJ = 0/40 Hrs. • Non-PJ = 0 Hrs. Project Alpha



Project Alphas > All Employee > All Roles

Name	Apr,2026				May,2026			
	06	13	20	23 (Today)	04	11	18	25
Nuntawan.P (June) • PM	100% 20/20 Hrs.	100% 20/20 Hrs.	100% 22/20 Hrs. (OT=2)	0% 0/48 Hrs.	0% 0/48 Hrs.	0% 0/40 Hrs.	0% 0/40 Hrs.	0% 0/40 Hrs.
MNO PQR (M) • SW Eng.					0% 0/40 Hrs.	0% 0/40 Hrs.	0% 0/40 Hrs.	0% 0/40 Hrs.

Project Beta > All Employee > All Roles

Name	Apr,2026				May,2026			
	06	13	20	23 (Today)	04	11	18	25
Nuntawan.P (June) • PM	140% 28/20 Hrs. (OT=8)							
ABC DEF (A) • PM		100% • PJ = 40/40 Hrs. • Non-PJ = 0 Hrs.	100% • PJ = 40/40 Hrs. • Non-PJ = 0 Hrs.	50% • PJ = 20/40 Hrs. • Non-PJ = 0 Hrs.	0% • PJ = 0/40 Hrs. • Non-PJ = 0 Hrs.			
MNO PQR (M) • SW Eng.					0% • PJ = 0/40 Hrs. • Non-PJ = 0 Hrs.	0% • PJ = 0/40 Hrs. • Non-PJ = 0 Hrs.	0% • PJ = 0/40 Hrs. • Non-PJ = 0 Hrs.	0% • PJ = 0/0 Hrs. • Non-PJ = 0 Hrs.

Remark



No	Topic	Data Source
1.	Plan and Actual of Resource Utilization	Timesheet
2.	Plan and Actual of Financing & Instalment Payment Status	ERP

- 
- The background of the slide features a dark, circular graphic with the letters 'TKC' in a bold, sans-serif font. To the left of the circle, a hand is shown pointing downwards. The background also includes a network diagram with nodes and lines, and a padlock icon. The text is white and bold, set against the dark background.
- **Any Helps Needed**
Any Questions
Any Concerns
Any Suggestions
